

GFWWTP – Phase 2 Project Update

City Council Update

March 2, 2026

Melanie Parvey, Water Works Director

Madison Alberts, Project Manager at PKG



Phase 2 Project Updates




Statistics

- Approved project cost \$85,898,291 (includes construction and engineering)
 - 75% complete
- Project started October 2023
- Approximately 50 crew members onsite across all trades
- PKG has worked 115,000 manhours with **ZERO** lost time incidents

Upcoming Milestones

- FSB operating level slab pour – March 20th
- Permanent power tie in to existing facility – May
- Populating membrane cassettes at MBR – late August
- Startup activities will begin this Fall

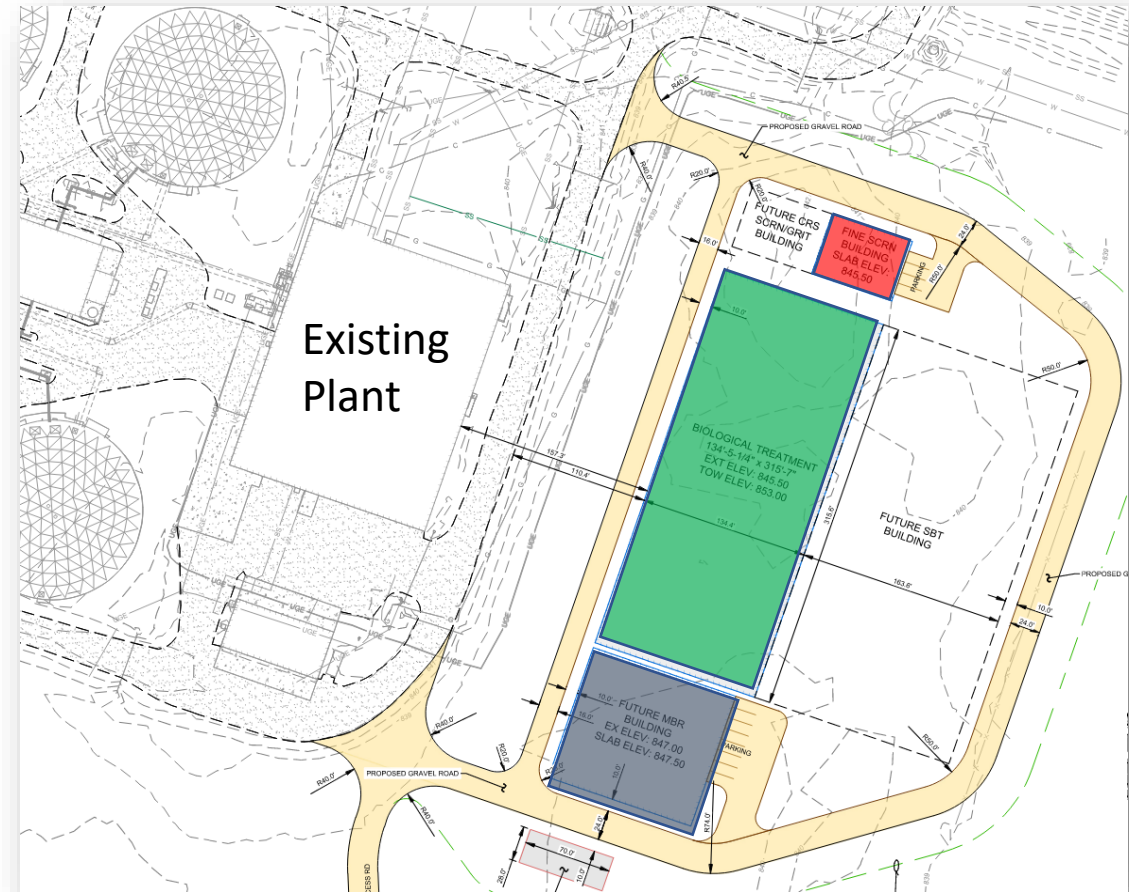

Phase 2 Progress



Fine Screen Building

- Start of treatment process
- Removal of solids and debris



Secondary Biological Treatment

- Removal of organic matter, suspended solids, nutrients

Membrane Bioreactor

- Advanced treatment
- Ability for water reuse

Phase 2 Progress





Current Progress

- Process piping ongoing throughout the facility
- Electrical installation ongoing throughout the facility
- HVAC/Plumbing work is 90% complete



Phase 2 will provide approximately 5 MGD additional treatment capacity with the ability for future expansion

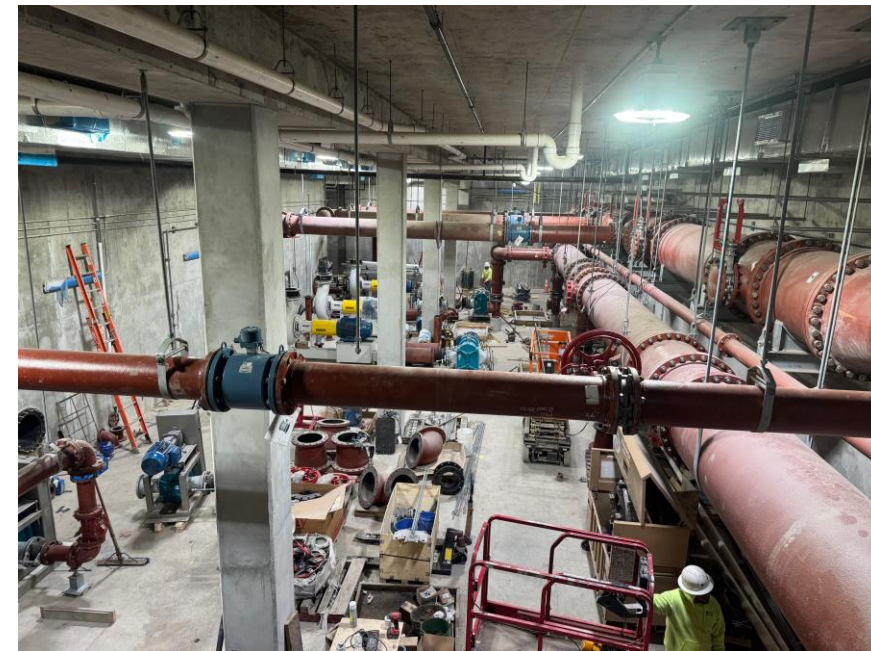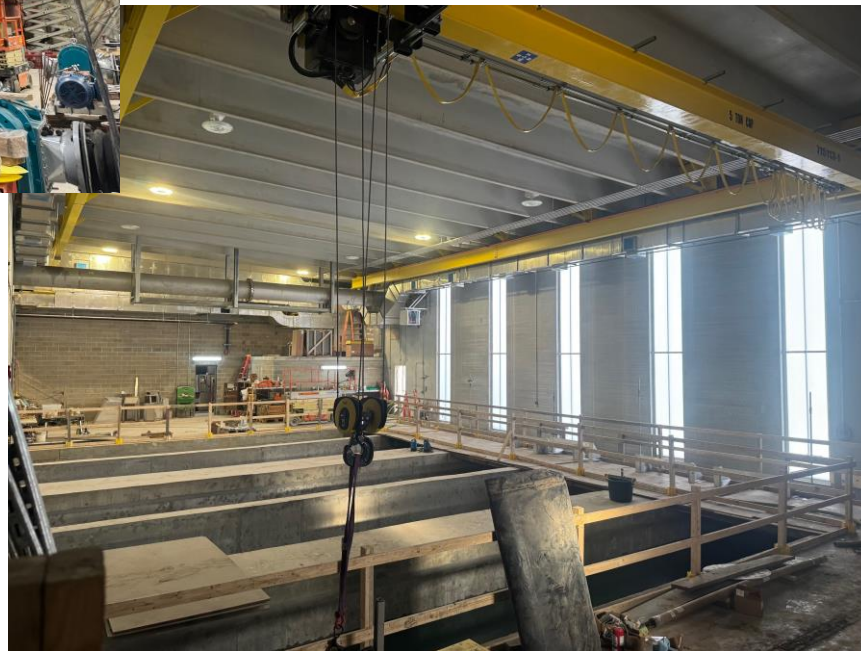

Phase 2 Progress



- Questions?
- Tours?

